



Qatargas 3&4 Upstream Safety Performance 4Q 2009 and 1Q 2010




Bill Mitchell
HSE Lead





Safety Performance 4Q 2009 & 1Q 2010

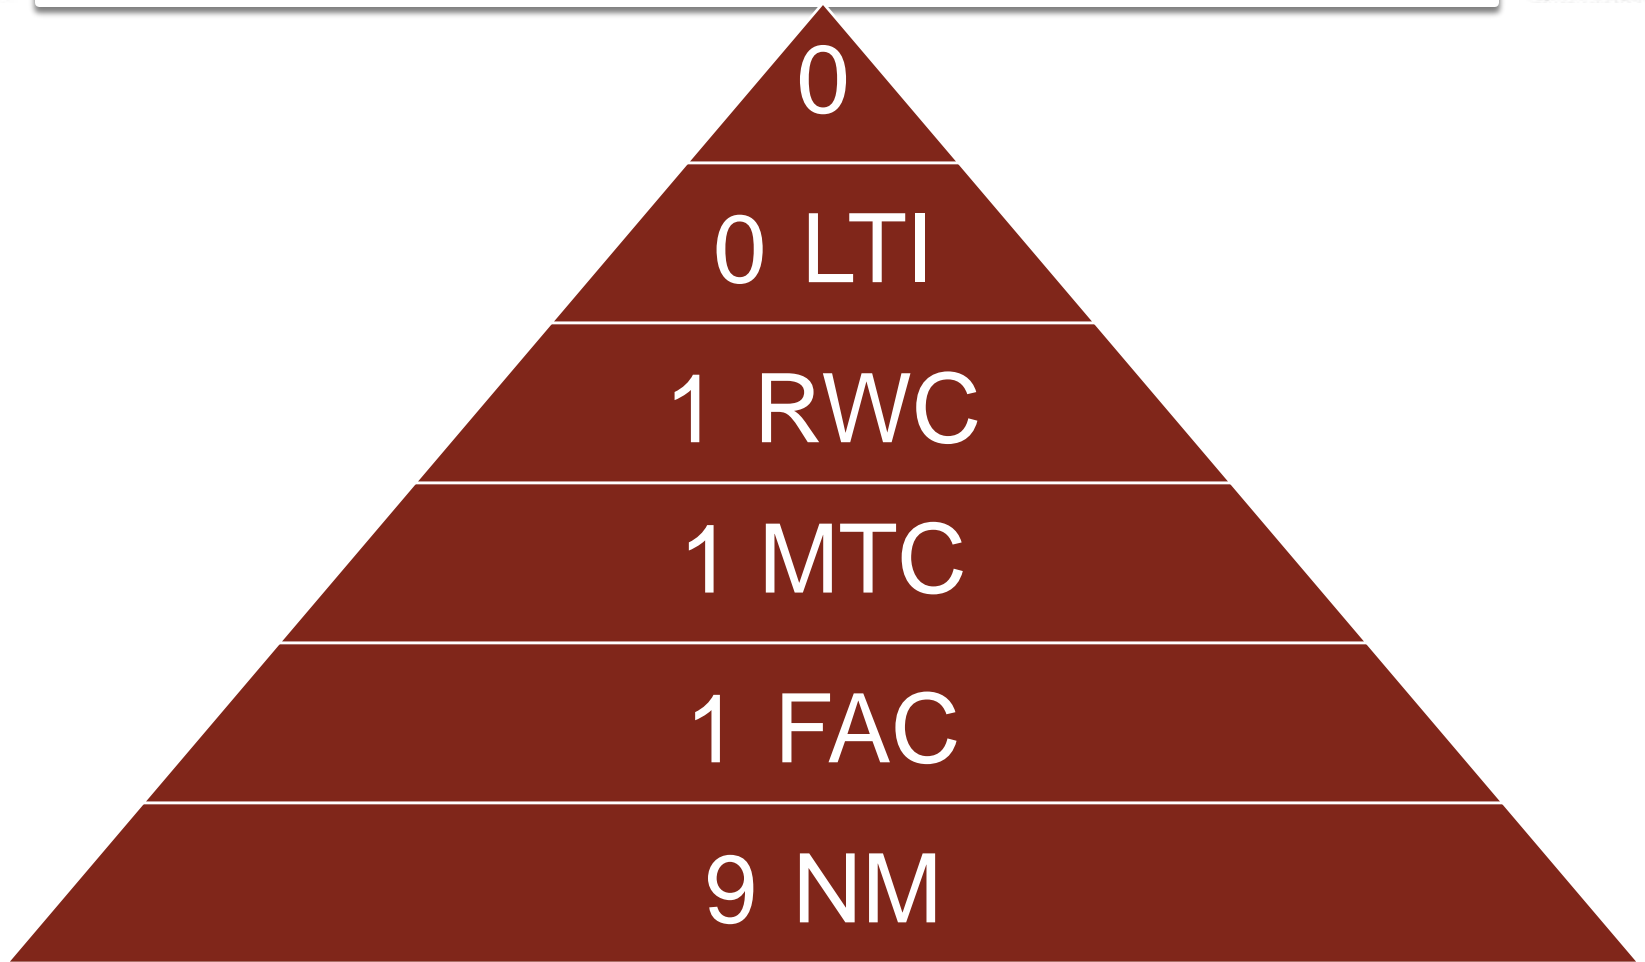



Safety Performance 4Q 2009 & 1Q 2010



Man hours Oct – Dec 2009	LTI	LTIR	TRI	TRIR
406,051	0	0	1	0.49

Manhours Jan – March 2010	LTI	LTIR	TRI	TRIR
382,287	0	0	1	0.52

Safety Performance 4Q 2009

Oct – Dec 2009 (Q4)

- **Recordable Incidents: 1**

MTC: Forehead laceration after hitting head on channel beam when walking to Muster on Al Khor.

Minor break to the skin – IP was treated with ant-tetanus injection and prescribed 5 days of prescription strength antibiotics





Safety Performance 1Q 2010



Jan – Mar 2010 (1Q)

- **Man-hours:** 382,287
- **Recordable Incidents: 1**
 - **RWC:** Fractured tip of R hand Ring Finger Chicksan coupling dropped on his hand when being backed off.

Other Incidents

- Near Miss x 3
 - Cascade Bottle Release of Air via ruptured Disc- Al Khor Rig
 - Wireline Drum on logging unit started to free fall allowing PLT Tool to drop down hole
 - Potential dropped joint Running String

- **Recordable Incidents**
- **RWC X 1**
- Fractured tip of Ring finger right hand. Injury occurred During rigging down of 4" 1502 chicksan lines in the high pressure pump room on the BO25. The IP was in the process of unscrewing the winged collar of the chicksan when the chicksan suddenly dropped and landed on the IP fingers on the deck of the pump room.



Wing which was disconnected

Chicksan which was rigged-down



Safety Performance 1Q 2010



Near Miss:

Free Fall of Wireline Drum on Logging unit allowed PLT Tool to drop down hole. No injuries.

Engine for unit turned off with the tool in the hole monitoring pressure build up.

Findings

- Cable Drum changed out 10 days earlier
- Brakes not readjusted/ rechecked or tested post change.
- Park Brake testing procedure unknown therefore not complied with



Safety Performance 1Q 2010



Near Miss:

Free Fall of Wireline Drum on Logging unit allowed PLT Tool to drop down hole. No injuries.

Engine for unit turned off with the tool in the hole monitoring pressure build up.

Findings

- Cable Drum changed out 10 days earlier
- Brakes not readjusted/ rechecked or tested post change.
- Park Brake testing procedure unknown therefore not complied with
